FIELD GUIDE

Understanding Structor AI

Marcel's preconstruction workflow, the Excel sheets, and the automation you promised

A plain-language guide for Danial Khan / Synix Solutions

THE ONE-SENTENCE VERSION Structor AI is meant to turn construction documents and subcontractor proposals into complete trade scopes, comparable bids, a defensible project budget, and eventually contract scope language.

Based on the 26 August 2026 discovery meeting and the Jelleff Recreation Center bid workbook

How to use this guide

Read Sections 1–4 first. They explain the business and workbook without assuming construction knowledge. Sections 5–8 explain the automation commitment and how the software should work. The final sections give you a practical checklist, questions for Marcel, and a glossary.

MOST IMPORTANT DISTINCTION The Excel workbook is the current container for Marcel's decisions. The real product is the process that creates those decisions and moves them from drawings to scopes, bids, budgets, and contracts.

Contents

- 1. The business in plain English
- 2. What Marcel actually does every day
- 3. The documents and construction vocabulary
- 4. What every workbook sheet means
- 5. A trade sheet explained cell by cell
- 6. Bid leveling with a worked example
- 7. What is manual, what Excel already automates, and what Structor should automate
- 8. What you actually promised Marcel
- 9. The recommended product milestones and data model
- 10. How the AI components should work safely
- 11. What you need from Marcel next
- 12. Meeting questions and glossary

1. The business in plain English

Marcel works in preconstruction for a general contractor. Preconstruction is the planning, pricing, and purchasing work performed before physical construction begins. His company must understand a proposed building well enough to tell the owner what it will cost and to buy the work from specialist subcontractors without leaving gaps.

Think of the general contractor as the company assembling the entire building. It usually does not personally manufacture every door, pour every slab, install every pipe, and wire every room. It hires separate specialist companies, called subcontractors, for those pieces of work.

The people involved

Party	What that party does
Owner / client	Pays for the project and defines the desired outcome.
Architect and engineers	Create drawings and specifications describing the building.
General contractor (GC)	Coordinates, prices, purchases, schedules, and manages the overall construction.
Bid captain	Leads the preconstruction bid, sets deadlines, assigns trades, and assembles the final price.
Estimator / division leader	Owns one or more trades, writes scopes, contacts bidders, levels bids, and recommends an award.
Subcontractor / sub	A separate specialist company bidding to perform one trade, such as concrete or electrical work.

What Marcel is really selling

He is not merely producing spreadsheets. He is producing confidence: confidence that the project scope is complete, that competing bids are comparable, that the budget does not hide missing work, and that the awarded contract clearly says what the subcontractor must provide.

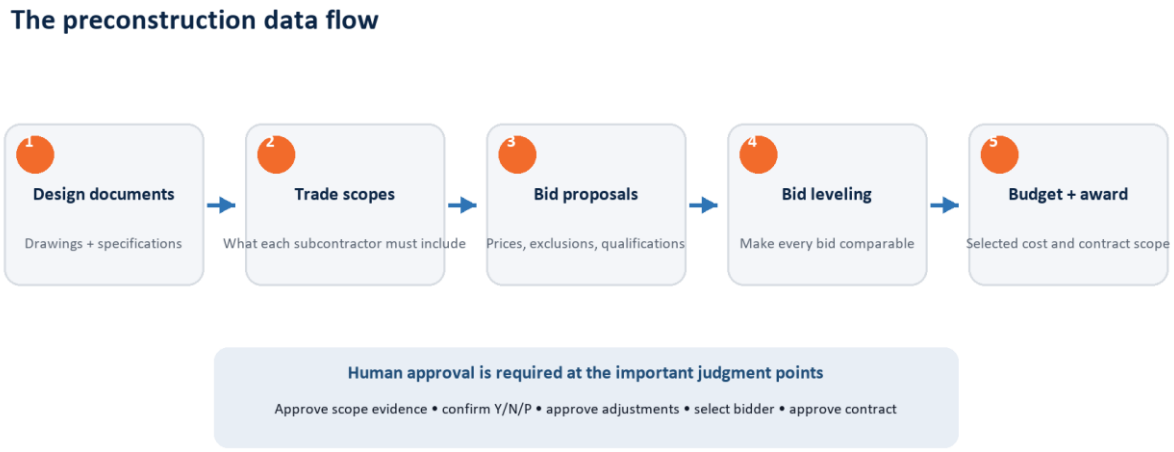


Figure 1. The entire preconstruction flow in one picture.

The central risk

A cheap-looking bid can be expensive if it excludes work that another bidder included. If nobody owns an item, the GC may discover the gap after the budget is committed. The missing work then becomes a cost overrun, dispute, or change order. Most of Marcel's process exists to prevent that outcome.

2. What Marcel actually does every day

The meeting described the following operational sequence. In practice, several steps overlap and different estimators work in parallel.

1. **Receive project documents.** The owner or architect provides drawings, specifications, reports, addenda, schedules, and instructions.
2. **Perform a drawing flip.** The bid captain reviews the set, identifies which CSI divisions and trades apply, and assigns them to estimators.
3. **Write one scope per trade.** Each estimator reads the relevant drawings and specifications and converts them into a checklist of everything that trade must include.
4. **Invite subcontractors.** The estimator sends the package to several qualified companies through BuildingConnected, email, or another outreach process.
5. **Answer questions and issue RFIs.** Subcontractors and estimators flag missing, unclear, or contradictory information before pricing is finalized.
6. **Receive proposals.** Each bidder returns a price plus inclusions, exclusions, allowances, alternates, and qualifications, usually by email.
7. **Level the bids.** The estimator compares each proposal against the same master scope, records Y/N/P, and adds internal adjustments for missing work.
8. **Select a value and update the budget.** The reviewed bid becomes the current expected cost for that trade; all trade values roll into the project total.
9. **Review scope and award.** The team meets with the preferred bidder, resolves remaining gaps, and makes an award recommendation.
10. **Create Exhibit A.** The approved scope is rewritten or formatted as the variable scope section of the subcontract.

Why it takes so long

Marcel said a drawing and specification package can contain roughly 1,000 to 5,000 pages. The team repeats the scope and leveling exercise across approximately 70 to 80 trades. The difficult work is not the addition formula; it is reading, classifying, comparing, and documenting thousands of facts and judgments.

What Marcel personally contributes

Marcel's contribution	Why software cannot blindly replace it
Trade ownership judgment	A note can appear on one drawing but belong contractually to a different trade.
Scope completeness	Generic scope language must be combined with project-specific details and coordination requirements.
Proposal interpretation	Subcontractor wording is inconsistent and may imply partial coverage rather than a clean yes or no.
Adjustment pricing	The cost of missing work depends on quantities, unit rates, market conditions, logistics, and risk.
Award recommendation	Price matters, but so do capability, schedule, qualifications, relationships, and commercial risk.
Contract judgment	An approved scope becomes a binding obligation and requires legal and operational review.

3. The documents and construction vocabulary

Drawings versus specifications

Drawings show where things are, their arrangement, dimensions, and relationships. The project manual or specifications explain materials, products, quality standards, execution requirements, testing, warranties, and other details. Marcel summarized the distinction as: drawings show what must be done; specifications explain how it must be done.

Source	Typical information	Example
Architectural drawings	Rooms, walls, doors, finishes, elevations, details	Where gypsum partitions and flooring occur
Structural drawings	Foundations, slabs, beams, columns, steel and reinforcing	Thickness and reinforcement of a concrete slab
Civil drawings	Grading, roads, exterior utilities, drainage and site work	Sanitary line from the street to the building
MEP/FP drawings	Mechanical, electrical, plumbing and fire-protection systems	Ductwork, power, piping and sprinkler layouts
Specifications / project manual	Products, standards, execution, submittals, warranties	Required manufacturer or concrete performance
Addenda and RFIs	Later clarifications or corrections	Architect confirms which of two conflicting details governs

Trade and CSI division

A trade is a package of work purchased from a specialist subcontractor. CSI numbers are standardized categories used to organize construction information. For example, the workbook uses 02 for demolition, 03 for concrete, 09 for finishes such as drywall and painting, 22 for plumbing, 23 for HVAC, and 26 for electrical.

IMPORTANT The CSI number helps organize information, but it does not automatically decide contractual responsibility. Scope crossover still requires human review.

Key terms before looking at Excel

Term	Meaning
Scope of work	The checklist or contract description of everything a trade must provide.

Term	Meaning
Proposal / bid	The subcontractor's submitted price and commercial qualifications.
Takeoff	A measured quantity from scaled drawings, such as 4,200 square feet of gym flooring.
RFI	Request for Information: a formal question raised because information is missing, unclear, or conflicting.
Alternate	An optional add or deduct price for a defined design choice.
Allowance	A placeholder amount for work whose final details or quantity are not yet known.
Value engineering (VE)	A proposal to reduce cost or improve value through an alternative material or method.
Exhibit A	The trade-specific scope attached to the subcontract and made contractually binding.

4. What every workbook sheet means

The Jelleff workbook is best understood as a small database disguised as Excel. Project records, trade records, scope items, bidders, responses, budgets, and decisions are stored in cells and linked by formulas.

The workbook has four kinds of sheets

Category	Sheets	Purpose
Project control	Bid Sheet; MCN Summary	Combines all trade costs into the project budget and summary.
Risk and coordination	ScopeCrossOver; RFI Log; VEs; Alternates; SpecMatrix	Tracks gaps, questions, options, and responsibility across trades.
Reusable structure	SOWTemplate; Version History	Provides the blank trade layout and tracks revisions.
Trade worksheets	Demo, Conc, GWB, HVAC, Elect, Plumb, and dozens more	Compares subcontractors for one trade at a time.

The important utility sheets

Sheet	Plain-English meaning	Data type
Bid Sheet	Master list of trades, CSI code, assigned estimator, old/current budget, variance, cost per GSF, and bidder values.	Output / control
MCN Summary	Rolls Bid Sheet values into standard CSI cost categories, total trades cost, construction cost, and cost per square foot.	Calculated summary
GCs n GRs	General Conditions and General Requirements: project staff, supervision, temporary facilities, safety, administration, and similar GC costs.	Inputs + formulas
SOWTemplate	Blank model for one trade: scope rows, internal budget, seven bidder groups, bond, totals, level state, and rank.	Reusable template
ScopeCrossOver	Records work that could be missed or counted twice because several trades could reasonably own it.	Human coordination
RFI Log	Stores question number, discipline, question, submission information, design response, and response date.	Human workflow
VEs	Logs value-engineering ideas and cost impact.	Human input
Alternates	Collects optional add/deduct prices by trade.	Input + summary

Sheet	Plain-English meaning	Data type
SpecMatrix	Maps specification sections and bid packages to assigned estimators and coverage.	Assignment / QA

Most other tabs are trades

Examples include Demo (demolition), Conc (concrete), Masonry, SS & MM (structural steel and miscellaneous metals), GWB (gypsum wallboard/drywall), DFH (doors, frames and hardware), Alum (aluminum/storefront), FireP (fire protection), Plumb, HVAC, Elect, LV (low voltage), EARTH, SiteConc, WetUtil, DryUtil, Lscape, and FFE.

5. A trade sheet explained cell by cell

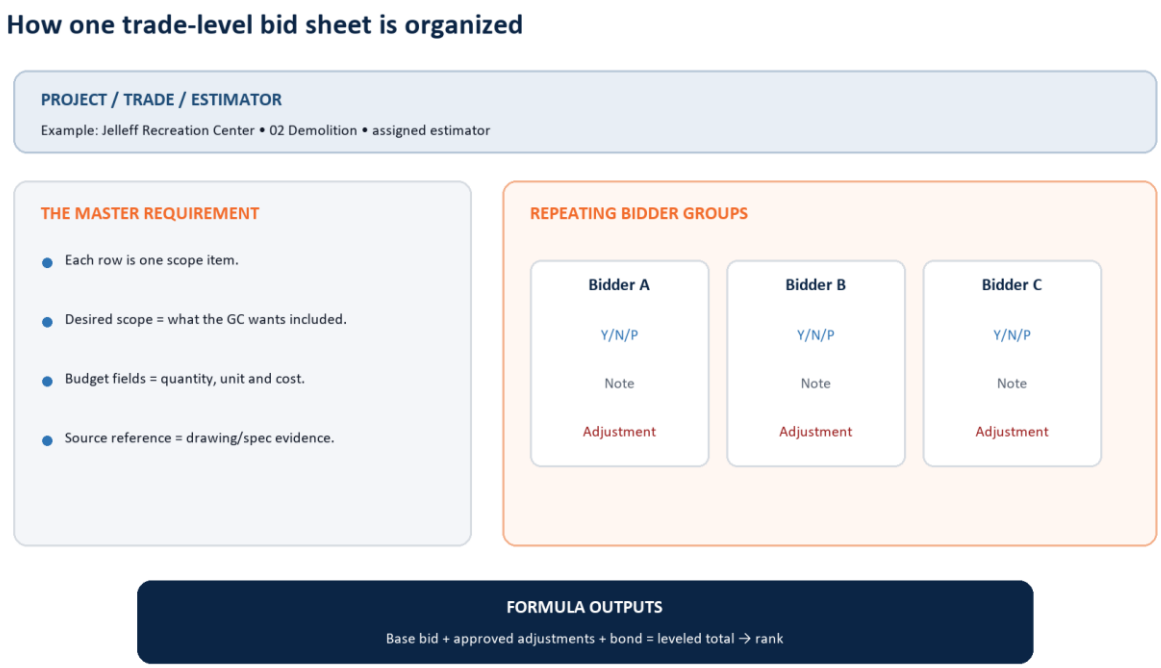


Figure 2. The anatomy of one trade sheet.

The top of the sheet

Field	Who supplies it	What it means
Project, bid date, trade, revision	Bid captain / project setup	Identifies the bid event and package.
Estimator contact	Project team	Person responsible for this trade.
Bidder company and contact	Proposal / bidder database	The subcontractor being compared.
Level Scope?	Estimator	Whether review is complete enough to calculate/rank.
Base Bid	Subcontractor proposal	The bidder's submitted starting price.
Adjustments	Estimator judgment	Internal amount added or deducted to make scope comparable.
Bond	Workbook formula	In the Jelleff template, 2% of base bid plus adjustments.
Total Bid and Rank	Workbook formula	Comparable total and position among completed bidders.

The left side: Marcel's requirement

Each scope row describes one required item. The Desired Scope column records what the GC wants—usually Y. The response/comment and internal MCN Budget fields can hold quantity, unit of measure, unit price, and cost.

Workbook field	Meaning
Scope Items to include	The master checklist the bidders must be compared against.
Desired Scope	Whether the GC expects the item to be included.
Response / Comment	Internal clarification or response associated with the requirement.
QTY	Quantity.
UOM	Unit of measure: SF, LF, CY, EA, LS, and similar units.
$/UOM	Expected cost per unit.
COST	Quantity multiplied by unit price.

The right side: the bidders

Every subcontractor receives the same three columns for every scope row. This is the heart of bid leveling.

Field	Meaning	Example
Y	Complete inclusion	Proposal clearly includes removal and disposal.
N	Excluded	Proposal says concrete footings are excluded.
P	Partial inclusion	Includes one mobilization, but the scope requires several.
Note	Reason and evidence	“Make-safe by others” or proposal page reference.
Adjustment	Internal cost needed to normalize the bid	$18,000 added for a missing second mobilization.

DO NOT CONFUSE THESE Desired Scope = what Marcel wants. Bidder Y/N/P = what a particular proposal appears to include. They answer different questions.

What the Jelleff demolition sheet contains

Bidder	Base bid	Workbook status	Cached total
Celtic Demo	$290,000	FULL SCOPE	$295,800
Marc's Demo	$240,000	FULL SCOPE	$244,800
ACECO	$358,597	FULL SCOPE	$365,769
Berg Demo	$154,826	FULL SCOPE	$157,923
D&H	$255,000	FULL SCOPE	$260,100
Rath	$260,000	NO	Not leveled

These values prove the workbook structure and formulas, but the file is not a complete truth set for automatic leveling: several bidder response columns are still blank, and the cached adjustment totals shown above are zero. Therefore, the lowest cached total should not be treated as an award recommendation without the completed scope review.

6. Bid leveling with a worked example

Bid leveling means converting differently scoped proposals into comparable internal totals. The following example is deliberately simplified and is not taken from the Jelleff bidder results.

The required demolition scope

Item	Master scope	Desired scope
1	Demolish existing building structure	Required
2	Remove foundations and footings	Required
3	Haul and legally dispose of debris	Required

Two proposals arrive

Comparison	Bidder A	Bidder B
Base bid	$290,000	$240,000
Building demolition	Y	Y
Foundations and footings	Y	N — excluded
Haul and disposal	Y	P — hauling only
Internal adjustment	$0	+$50,000
Subtotal before bond	$290,000	$290,000
2% bond	$5,800	$5,800
Leveled total	**$295,800**	**$295,800**

THE LESSON Bidder B looked $50,000 cheaper, but only because important work was missing. After leveling, both bids cost the GC the same amount.

The formula in Marcel's template

Leveled total = (Base bid + Approved adjustments) × 1.02

The 1.02 factor represents the workbook's 2% bond. Other companies or projects may use different rules, so the percentage must be a visible project setting—not hard-coded into the future product.

Why the lowest bid does not automatically win

- The low bidder may have exclusions or qualifications.
- The bidder may lack capacity, manpower, schedule availability, bonding, or relevant experience.
- The scope may still be ambiguous or dependent on an unanswered RFI.
- The estimator may prefer a slightly higher bidder with a cleaner and more reliable proposal.
- The final award must reflect scope-review and commercial negotiations, not only a rank formula.

7. What is manual, what Excel already automates, and what Structor should automate

Activity	Today	Future Structor behavior
Read drawings/specifications	Manual specialist review; Wyre AI used as reference tool	Draft trade scopes with page/detail/spec citations.
Write scope rows	Estimator writes or edits Excel/PDF scope	Suggest project-specific and library-based rows; human approves.
Enter bidder/contact/base bid	Typed from email and proposal	Extract from uploaded proposal or dedicated bid inbox.
Mark Y/N/P	Estimator reads proposal row by row	AI drafts status with exact proposal evidence; human confirms.
Write notes	Manual	Draft concise note from proposal exclusion or qualification.
Estimate adjustment	Estimator judgment	Suggest quantity × unit rate or historical allowance; require approval.
Bond, total, rank	Excel formulas	Deterministic calculation service using visible project rules.
Update Bid Sheet / summary	Linked cells and manual review	Automatic approved roll-up with audit trail.
Create Exhibit A	Copy/rewrite approved scope	Generate from approved scope and project template; legal review required.

The key insight

THE PRODUCT IS NOT AN EXCEL CLONE Excel already performs the arithmetic. Structor's value is extracting, organizing, comparing, citing, reviewing, and reusing the information that humans currently type into Excel.

What the current prototype does

The prototype imports the Jelleff Demo or SOWTemplate tab, reads project/trade metadata, scope rows, bidder names, base bids, Y/N/P, notes and adjustments, calculates the 2% bond and leveled totals, supports review, and exports changes back into Excel. It demonstrates the workflow shell, not the finished AI intelligence.

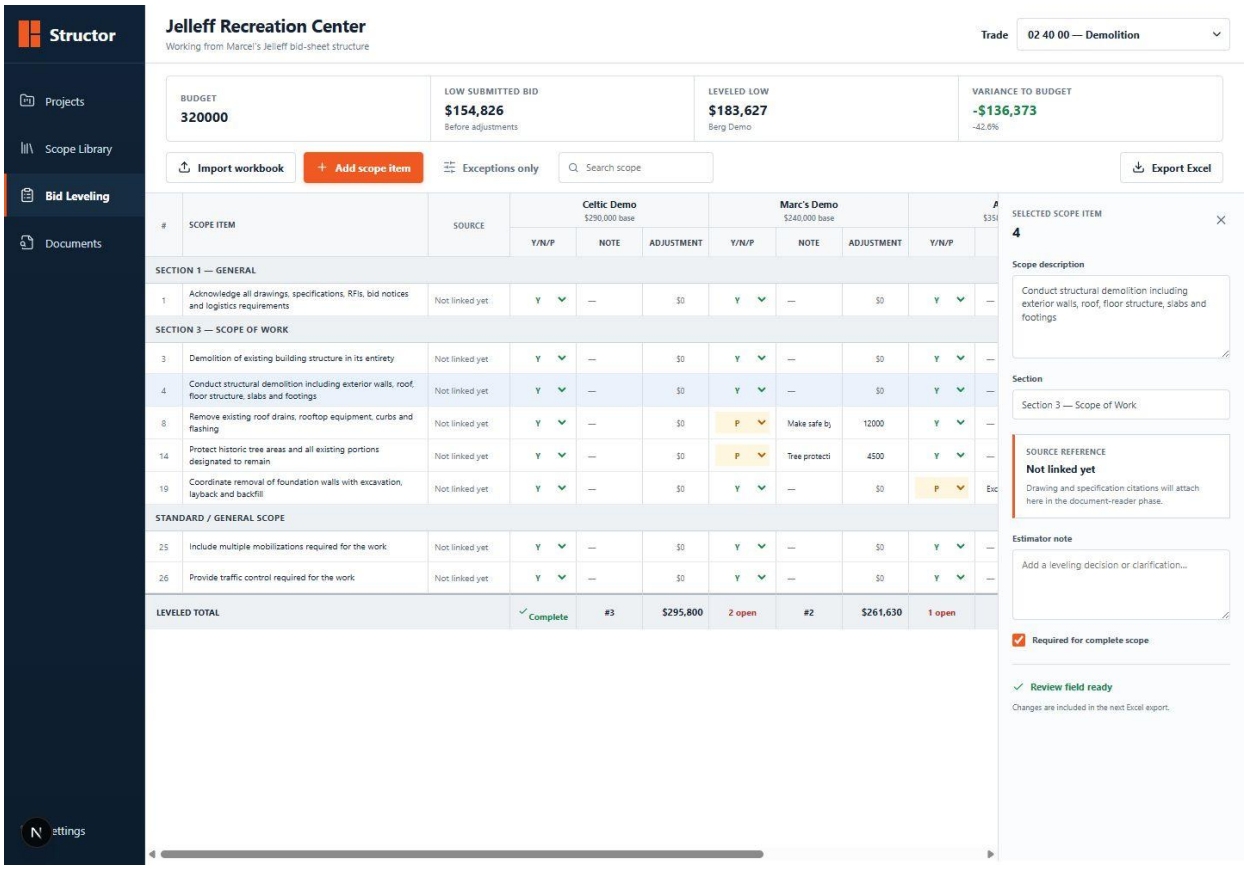


Figure 3. Current Structor workflow prototype using the Jelleff demolition structure. Some interface adjustment examples are illustrative, not source-of-truth workbook values.

What the prototype does not yet do

- Read construction drawings or specifications.
- Generate scope rows with citations.
- Parse real subcontractor proposal PDFs.
- Decide Y/N/P from evidence.
- Suggest defensible adjustment amounts from quantities and unit costs.
- Operate a dedicated bid inbox or subcontractor portal.
- Generate final contracts or takeoffs.

8. What you actually promised Marcel

The meeting contains several ideas, but the immediate commitment was narrower than the long-term vision. It is important not to combine every requested feature into a one-week promise.

The immediate commitment for the next meeting

Commitment	Meaning
Domain research	Understand the terminology, document types, trade codes, and where information flows.
A basic front-end demo	Show what the web application could look like so Marcel can give workflow feedback.
A sheet-filling application	Prototype an application that populates the existing trade-sheet structure.
Excel export	Preserve Marcel's familiar workbook output.
Iterative review	Meet weekly, ask informed questions, and refine the interface and workflow.

EXACT BOUNDARY You estimated that the sheet prototype and demo could be ready by the following meeting. You did not promise a production-ready drawing-reading AI, automatic takeoffs, or a fully autonomous estimator within one week.

The broader capability you said was possible

You also agreed that the product could eventually extract construction information from blueprints, organize it by universal construction codes, show scopes as notes with source references, and export a trade file. That was agreement on technical direction, not a one-week completion date.

There were two different 'Step 1' statements

Whose Step 1?	What it meant	Correct interpretation
Marcel's product Step 1	Upload drawings/specifications and generate cited scopes by trade.	The first major AI capability and the hardest intelligence problem.
The team's implementation starting point	Build the interface and automate sheet population/export.	The easiest demonstrable prototype and the actual next-meeting commitment.

What 'automate the sheets' should mean

- Create or populate a trade sheet from structured project, scope, and bidder data.
- Accept scope rows from manual entry first, then from the drawing reader later.
- Accept bidder data from manual entry first, then proposal/email extraction later.
- Calculate adjustments, bond, leveled total, completion state, and rank consistently.
- Update the master Bid Sheet only after human approval.
- Export a workbook that preserves the expected layout and opens without repair warnings.

9. The recommended product milestones and data model

Milestone 1 — Workflow and Excel prototype

This is the current stage: project setup, trade selection, structured scope rows, bidder values, review controls, deterministic leveling calculations, and Excel export. It proves that the product can reproduce Marcel's operating surface without waiting for complex document AI.

Milestone 2 — First true AI scope pilot

Use one bounded trade—recommended: Jelleff drywall. Upload the relevant drawing/specification subset, generate a draft scope, attach a citation to every project-specific item, let Marcel accept/edit/reject it, and export the approved result.

Milestone 3 — Proposal ingestion and auto-leveling

Parse a real bidder proposal, identify the project/trade/bidder, extract base price, exclusions, alternates and qualifications, compare the proposal with the approved scope, and draft Y/N/P, notes, and missing-scope flags for approval.

Milestone 4 — Roll-up, contract, and operations

Move approved values into the project budget, generate Exhibit A from the approved scope, and add RFI, VE, alternate, assignment, audit, and handoff workflows. Takeoffs and subcontractor-side pricing can follow as separate, measurable products.

The data model behind Excel

Record	Important fields
Project	Name, client, location, dates, area, revision, source documents
Trade	CSI code, trade name, assigned estimator, project budget
Scope item	Section, text, required flag, source citation, review status
Bidder	Company, contact, email, phone, qualification data
Proposal	File, bidder, trade, submitted price, alternates, exclusions
Bid response	Scope item × bidder: Y/N/P, note, evidence, adjustment, approver
Leveling result	Base bid, adjustment total, bond, leveled total, completeness, rank
Decision	Recommended/selected bidder, approved budget value, rationale

Record	Important fields
Award document	Approved scope converted to Exhibit A / contract language

WHY THIS MATTERS Once these records exist separately from Excel, the same approved data can power the web app, Excel export, project summary, scope library, audit history, and contract without copying information repeatedly.

10. How the AI components should work safely

A. Drawing and specification reader

1. Ingest each file and preserve page, sheet number, discipline, revision, and document type.
2. Extract text, schedules, notes, callouts, details, and specification sections while retaining coordinates.
3. Classify facts into likely trades and CSI sections.
4. Generate draft scope sentences from the evidence and reusable scope library.
5. Attach the exact drawing/specification citation and preview region to every project-specific scope item.
6. Require a reviewer to accept, edit, reject, or reassign each item.

B. Proposal reader

1. Identify project, trade, bidder, proposal date and revision.
2. Extract base bid, taxes/bond assumptions, exclusions, alternates, allowances and qualifications.
3. Compare proposal language to each approved master scope row.
4. Draft Y/N/P and a concise note with the exact proposal evidence.
5. Flag unresolved or contradictory language instead of guessing.
6. Let the estimator approve the comparison before it affects totals or the budget.

C. Adjustment suggestion

The system can suggest an adjustment when a bidder misses work, but this must be explainable. A useful suggestion shows the missing quantity, unit of measure, selected unit rate, rate source, calculation, confidence, and who approved it. A black-box number is not acceptable for a bid or contract.

D. Scope and cost library

The library should remember approved, reusable knowledge—not silently train on every draft. Store standard scope clauses by trade, project-specific approved clauses, drawing/specification citation patterns, historical unit costs with date/location context, proposal terminology, and approved adjustment decisions. Every reuse should show provenance.

Non-negotiable safeguards

Safeguard	Required behavior
Evidence	Every non-generic extracted fact links back to its source.
Human approval	AI suggestions do not automatically alter the budget or contract.
Revision awareness	A drawing/spec revision can invalidate earlier citations and decisions.
Audit trail	Store who changed Y/N/P, adjustment, selection, and contract scope, and when.
Clean-room implementation	Do not copy Wyre AI code, private prompts, protected templates, or NDA-restricted behavior.
Security	Drawings, bids and contracts are commercially sensitive and require tenant isolation and access controls.

11. What you need from Marcel next

DO NOT ASK FOR RANDOM MOCK SHEETS Ask for one matched, completed trade package from source documents through final decision. The files must tell one coherent story.

The recommended golden dataset

- The exact drawing and specification files used for the bid.
- The final human-written trade scope or bid form.
- At least two or three subcontractor proposals for that trade.
- The completed leveling sheet with Y/N/P, notes and adjustments.
- RFIs, addenda or clarifications that changed the scope.
- The selected bidder and approved budget value.
- The final Exhibit A, if one was issued.

Best first pilot: Jelleff drywall

The verified source inventory indicates that drywall is the strongest complete test case: drawings and project manual, a human drywall scope/bid form, a District bid form and proposal, the populated GWB sheet, and a Wyre AI sample package. Demolition is useful for understanding workbook formulas, but the shared drywall package is better for testing the whole chain.

What you should ask Marcel to label

Labeling task	Question to answer
For each scope item	Which drawing page/detail or specification section created it? Is it standard or project-specific?
For trade ownership	Why does this item belong to drywall/concrete/etc. and not another trade?
For each proposal	Which sentence supports Y, N or P? What does ambiguous wording mean?
For each adjustment	What quantity, unit rate and judgment created the amount?
For the decision	Why was the preferred bidder selected? What non-price factors mattered?
For the output	Which values moved to the Bid Sheet, budget and Exhibit A?

Your role in the automation

You do not need to become a senior estimator before building anything. Your job is to make the decision process explicit: identify the input, capture the output, record the evidence and approval, and translate repetitive actions into software. Marcel remains the domain owner who validates whether the output is commercially correct.

12. Questions for the next meeting

1. Which exact project and trade are we using as the first acceptance test?
2. Is the next deliverable sheet population only, or must it parse a proposal PDF?
3. Which workbook is the production template, and which formulas/formatting must be preserved exactly?
4. What does FULL SCOPE mean operationally, and who is allowed to set it?
5. Can Y/N/P be entered by the subcontractor, the estimator, AI, or all three?
6. What evidence is sufficient to mark Y? What conditions require P instead?
7. How are missing-scope adjustments calculated today?
8. Does bond always apply to base bid plus adjustments, and is 2% configurable?
9. When are allowances and alternates included in the leveled total?
10. Which bidder value is copied into the Bid Sheet: lowest leveled, selected bidder, or manual budget?
11. What must be completed before a bidder can be ranked?
12. Which proposal formats and email patterns are most common?
13. What may legally be used from Wyre AI and the prior development team?
14. Who approves scopes, adjustments, budget values and Exhibit A?
15. What measurable accuracy would make the first AI pilot successful?

A 30-second explanation you can repeat

SCRIPT Marcel receives construction drawings and needs to buy dozens of specialist trades. He writes a checklist for each trade, receives several proposals, and compares every proposal against the same checklist so a cheap bid cannot hide missing work. Today that comparison is entered manually into Excel. We are building a web app that structures the data, helps read drawings and proposals, drafts the comparison with evidence, calculates the leveled totals, and exports the approved result back to his workbook and eventually the contract.

Glossary

Term	Plain-English definition
Addendum	A formal change or clarification issued during bidding.

Term	Plain-English definition
Allowance	A placeholder amount for uncertain or not-yet-defined work.
Alternate	A separately priced optional add or deduct.
Base bid	The subcontractor's primary submitted price before internal leveling adjustments.
Bid captain	The person coordinating the overall project estimate and bid process.
Bid leveling	Making proposals comparable against the same required scope.
Bond	Financial security cost applied according to project/company rules; 2% in the Jelleff template.
CSI division	Standard construction category used to organize work and specifications.
Exclusion	Work the bidder explicitly says is not included.
Exhibit A	The subcontract's trade-specific scope attachment.
GC	General contractor.
GCs / GRs	General Conditions and General Requirements: the GC's project-management and jobsite costs.
GSF	Gross square feet of the project.
Leveled total	Comparable internal total after approved adjustments and bond rules.
Proposal qualification	A condition or assumption limiting the bidder's offer.
RFI	Request for Information.
Scope crossover	Work whose trade ownership is ambiguous or shared.
Scope item	One requirement in a trade's master checklist.
Subcontractor	Specialist company performing one part of the construction.
Takeoff	Measured quantity derived from scaled drawings.
Trade	A package of related construction work purchased from a specialist.
UOM	Unit of measure, such as SF, LF, CY, EA or LS.
VE	Value engineering.
Y/N/P	Included / not included / partially included.

Sources and limitations

This guide was prepared from the timestamped Zoom transcript for the 26 August 2026 discovery meeting, the Jelleff Rec Live Bid sheet.xlsx workbook, the verified shared-source inventory, and the current Structor prototype documentation. Workbook formulas and cached values were inspected directly.

The local MP4 recording could not be opened through the available browser because local-file playback was blocked by security policy, and the in-app Drive session required sign-in. Therefore, exact claims about the meeting are based on the complete timestamped transcript rather than unverified visual inference. The workbook and locally retained project materials were inspected directly.

Some transcript speaker labels appear imperfect, especially where a statement addressed to Marcel is labeled as Marcel speaking. Requirements are attributed by substance rather than assuming every speaker tag is exact.

Source	Used for
Zoom transcript	Meeting statements, terminology, requested product capabilities, and commitments; 18:02–18:38.
Jelleff Rec Live Bid sheet.xlsx	Workbook sheets, formulas, bidder structure, budget roll-ups, RFI log, and trade tabs.
SOURCE_MATERIALS.md	Verified shared-folder inventory dated 31 August 2026 and recommended golden dataset.
README.md	Current prototype boundary, implementation status, roadmap, and source caveats.
